


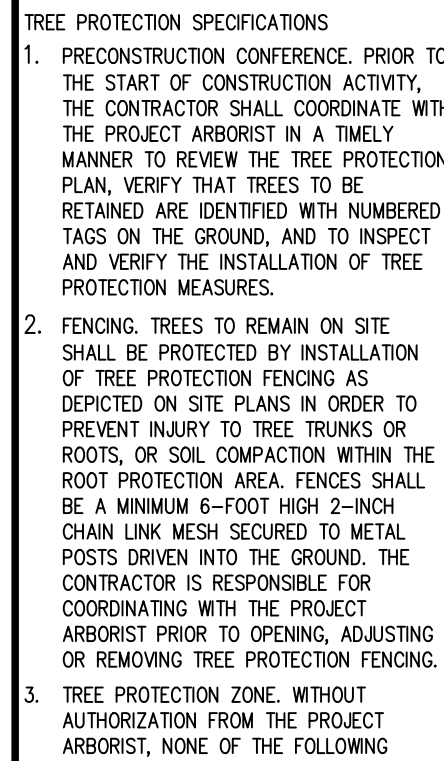

THE CONTRACTOR SHALL BE RESPONSIBLE FOR CONTACTING THE PROJECT ARBORIST IN A TIMELY MANNER PRIOR TO WORKING BENEATH PROTECTED TREE DRIPLINES. ROOT PROTECTION ZONES MAY BE ENTERED FOR TASKS LIKE SURVEYING, MEASURING AND SAMPLING. FENCES MUST BE CLOSED UPON COMPLETION OF THESE TASKS.

TREE AND STUMP REMOVAL. TREES TO BE REMOVED SHALL BE CLEARLY IDENTIFIED WITH TREE-MARKING PAINT OR OTHER METHODS APPROVED IN ADVANCE BY THE PROJECT ARBORIST. PROTECTION FENCING MAY BE TEMPORARILY OPENED IN TRACT FOR REMOVAL OF TREES #6564 AND


5. PRUNING. PRUNING MAY BE NEEDED TO PROVIDE OVERHEAD CLEARANCE AND TO REMOVE DEAD AND DEFECTIVE BRANCHES FOR SAFETY. THE PROJECT ARBORIST CAN HELP IDENTIFY WHERE PRUNING IS NECESSARY ONCE TREES RECOMMENDED FOR REMOVAL HAVE BEEN REMOVED AND THE SITE IS PREPARED FOR CONSTRUCTION. TREE REMOVAL AND PRUNING SHALL BE PERFORMED BY A QUALIFIED TREE SERVICE.

6. EXCAVATION AND ROOT PRUNING.  
EXCAVATION BENEATH PROTECTED TREE DRUPINES SHALL BE AVOIDED IF ALTERNATIVES ARE AVAILABLE. IF EXCAVATION IS UNAVOIDABLE, THE PROJECT ARCHITECT SHALL EVALUATE THE PROPOSED EXCAVATION TO DETERMINE METHODS TO MINIMIZE IMPACTS TO TREES. ROOT PRUNING SHALL BE LIMITED AND DOCUMENTED BY THE PROJECT ARCHITECT.
7. LANDSCAPING FOLLOWING CONSTRUCTION AND WHERE LANDSCAPING IS DESIRED, APPROXIMATELY 3-INCHES OF THE TOP OF THE TRUNK OF PROTECTED TREES IN A MINIMUM 5-FOOT RADIUS AROUND TREE TRUNKS, DO NOT PILE MULCH DIRECTLY AGAINST TREE TRUNKS. MULCH AND COVERED PLANTS MAY BE PLANTED WITHIN THE GRASS-FREE MULCH RINGS. IF IRRIGATION IS USED, USE DRIP IRRIGATION ON LOW FLOW EMITTERS INSTALLED AT 18 INCHES GRADE. NO TREE PRUNING OR LOW MAINTENANCE DRUPINES OF PROTECTED TREES. LANDSCAPING SHALL BE PERFORMED BY THE CONTRACTOR WITH HAND TOOLS. ADEQUATE PROTECTED TREE DRUPINES, BENEATH THE LOCATION OF PLANTS TO

8. AVOID TREE ROOT IMPACTS.
9. QUALITY ASSURANCE. A QUALIFIED ARBORIST SHOULD SUPERVISE PROPER EXECUTION OF THIS PLAN ON-CALL DURING CONSTRUCTION ACTIVITIES THAT COULD ENCROACH ON RETAINED TREES. TREE PROTECTION SITE INSPECTION MONITORING REPORTS SHOULD BE PROVIDED TO THE CLIENT AND CITY FOLLOWING EACH SITE VISIT PERFORMED DURING CONSTRUCTION.
9. REASSESSMENT. TREES THAT ARE RETAINED WITH SITE IMPROVEMENT WORK SHALL BE REASSESSED IN TERMS OF FUTURE HOME PLANS. ADDITIONAL TREE REMOVAL OR ALTERNATIVE TREE PROTECTION MEASURES MAY BE NEEDED

9. REASSESSMENT. TREES THAT ARE RETAINED WITH SITE IMPROVEMENT WORK SHOULD BE REASSESSED IN TERMS OF FUTURE HOME PLANS; ADDITIONAL TREE REMOVAL OR ALTERNATIVE TREE PROTECTION MEASURES MAY BE NEEDED.

|                                                                                       |           |
|---------------------------------------------------------------------------------------|-----------|
|  | GOOD      |
|  | FAIR      |
|  | POOR      |
|  | VERY POOR |



| TREE # | SPECIES  | DBH* | REMOVE |
|--------|----------|------|--------|
| 3226   | OAK      | 12   | REMOVE |
| 3227   | OAK (x2) | 12   | REMOVE |
| 3228   | OAK      | 32   | REMOVE |
| 3229   | OAK      | 12   | REMOVE |
| 3230   | OAK      | 10   | REMOVE |
| 3231   | OAK      | 8    | REMOVE |
| 3232   | OAK      | 16   | REMOVE |
| 3233   | OAK      | 12   | REMOVE |
| 3234   | OAK      | 8    | REMOVE |
| 3235   | OAK (x2) | 12   | REMOVE |
| 3236   | OAK      | 8    | REMOVE |
| 3237   | OAK      | 8    | REMOVE |
| 3238   | OAK      | 16   | REMOVE |
| 3239   | FIR      | 8    | REMOVE |
| 3240   | OAK      | 10   | REMOVE |
| 3241   | OAK (x2) | 16   | REMOVE |
| 3242   | OAK (x3) | 16   | REMOVE |
| 3243   | OAK (x3) | 16   | REMOVE |
| 3244   | OAK (x5) | 14   |        |
| 3245   | OAK      | 14   |        |
| 3246   | OAK (x2) | 16   |        |
| 3247   | OAK      | 15   |        |
| 3248   | OAK      | 18   |        |
| 3249   | OAK (x2) | 12   |        |
| 3250   | OAK      | 16   |        |
| 3251   | OAK      | 24   |        |
| 3252   | OAK      | 14   | REMOVE |
| 3253   | OAK      | 8    | REMOVE |
| 3254   | OAK      | 10   | REMOVE |
| 3255   | OAK      | 8    | REMOVE |
| 3256   | OAK      | 10   | REMOVE |
| 3257   | OAK      | 8    | REMOVE |
| 3258   | OAK      | 8    | REMOVE |
| 3259   | OAK      | 12   | REMOVE |
| 3260   | OAK      | 14   | REMOVE |
| 3261   | OAK (x3) | 12   | REMOVE |
| 3262   | OAK      | 10   | REMOVE |
| 3263   | OAK (x3) | 10   | REMOVE |
| 3264   | OAK      | 10   | REMOVE |
| 3265   | OAK      | 16   | REMOVE |
| 3266   | OAK      | 16   |        |
| 3267   | OAK      | 10   |        |
| 3268   | OAK      | 16   | REMOVE |
| 3269   | OAK      | 10   | REMOVE |
| 3270   | OAK      | 18   | REMOVE |
| 3271   | OAK (x3) | 12   | REMOVE |
| 3272   | OAK (x2) | 12   |        |
| 3273   | OAK      | 18   |        |
| 3274   | OAK      | 10   |        |
| 3275   | OAK (x2) | 18   |        |
| 3276   | OAK      | 12   |        |
| 3277   | OAK      | 22   |        |
| 3278   | OAK      | 10   |        |
| 3280   | OAK      | 18   |        |
| 3281   | OAK (x2) | 16   |        |
| 3282   | OAK      | 8    |        |
| 4466   | OAK      | 30   |        |
| 4467   | OAK      | 18   |        |
| 4468   | OAK      | 24   |        |
| 4469   | OAK      | 22   |        |
| 4470   | OAK      | 24   |        |
| 4471   | FIR      | 36   |        |
| 4472   | OAK      | 24   |        |
| 4473   | OAK      | 24   |        |
| 4474   | OAK      | 14   |        |
| 4500   | OAK      | 36   |        |
| 4565   | OAK      | 18   |        |
| 4566   | FIR      | 36   |        |
| 4567   | OAK      | 14   |        |
| 4568   | FIR      | 16   |        |
| 4569   | OAK      | 20   |        |
| 4570   | OAK      | 14   |        |
| 4571   | OAK      | 20   |        |
| 4572   | OAK      | 19   |        |
| 4573   | OAK      | 18   |        |
| 4574   | OAK      | 28   |        |
| 4575   | OAK      | 22   |        |
| 4576   | OAK      | 20   |        |
| 4577   | OAK      | 12   |        |
| 4578   | OAK      | 18   |        |
| 4579   | OAK      | 14   |        |
| 4580   | OAK      | 18   |        |
| 4581   | OAK      | 14   |        |
| 4582   | OAK      | 14   |        |
| 4583   | OAK      | 12   |        |
| 4584   | OAK      | 10   |        |
| 4585   | OAK      | 12   |        |
| 4586   | OAK      | 10   |        |
| 4587   | OAK      | 12   |        |
| 4588   | OAK      | 8    |        |
| 4589   | OAK (x2) | 12   |        |
| 4590   | OAK (x2) | 16   |        |
| 4594   | FIR      | 18   | REMOVE |
| 4595   | FIR      | 18   | REMOVE |
| 4596   | FIR      | 20   | REMOVE |
| 4597   | FIR      | 22   | REMOVE |
| 4598   | FIR      | 20   | REMOVE |
| 4599   | FIR      | 18   | REMOVE |
| 4600   | FIR      | 20   | REMOVE |
| 5461   | FIR      | 8    |        |

| TREE # | SPECIES | DBH* | REMOVE |
|--------|---------|------|--------|
| 5462   | FIR     | 8    |        |
| 5463   | FIR     | 8    |        |
| 5464   | FIR     | 8    |        |
| 5466   | FIR     | 8    |        |
| 5468   | FIR     | 8    |        |
| 5469   | FIR     | 8    |        |
| 5470   | FIR     | 8    |        |
| 5472   | FIR     | 8    |        |

DBH\* DIAMETER AT BREAST HEIGHT, INCHES.

 INDICATES OFFSITE TREE, OR TREE NOT LOCATED WITHIN PROJECT AREA. NOT INCLUDED IN TREE PRESERVATION COUNT.

4540 PRINGLE RD SE  
TAX MAP - 3000 & 3002  
TAX MAP - 083W11BC  
SW1/4 NW1/4 SEC11 T8S R3W W.M.  
SALEM, OREGON

# TREE PRESERVATION AND REMOVAL PLAN - SOUTHWEST

[illegible]

**EMERIO**  
ENGINEERING • SURVEYING • DESIGN  
2887 WILLAMETTE ROAD, SUITE 1A  
EUGENE, OREGON 97401  
TEL: (503) 746-5812  
FAX: (503) 639-9592  
www.emeriodesign.com

REGISTERED PROFESSIONAL  
ENGINEER  
NO. 10000  
EXPIRES: 6/30/2023

**P3.3** OF **32**
